
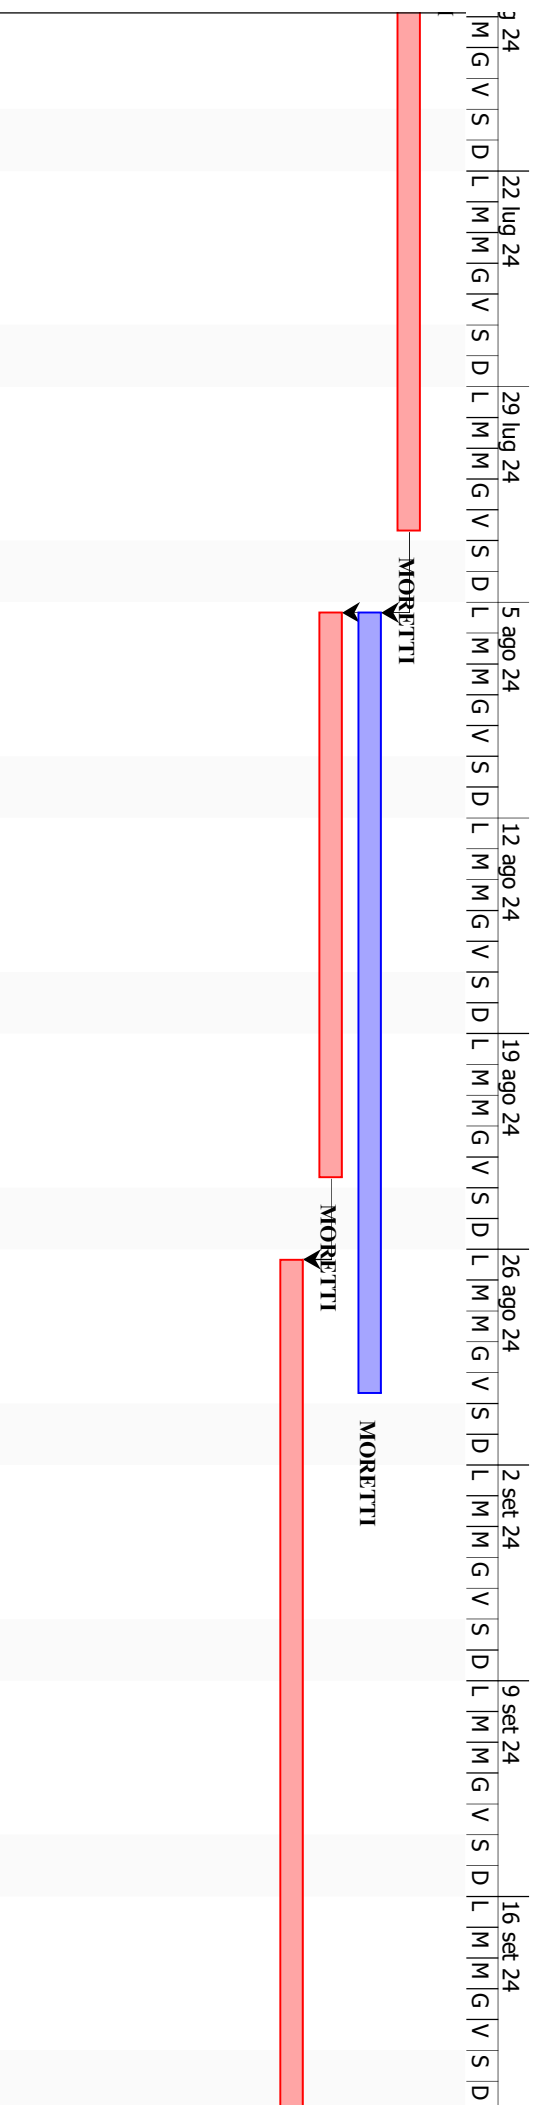
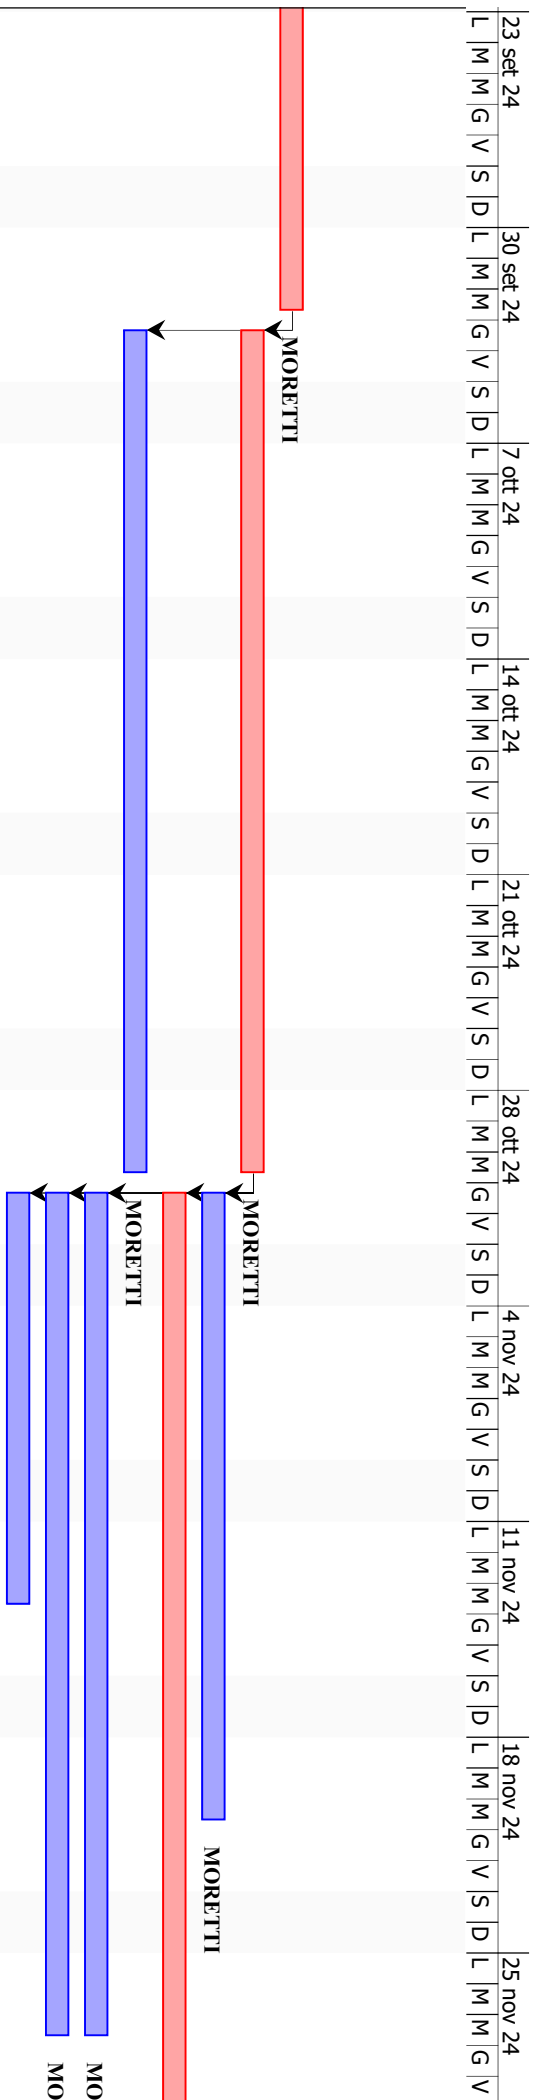


		Nome	Durata	Data di Avvio	Data di chiusura	Predecessori	Nome risorsa	D	L	M	M	G
1		ACCANTIERAMENTO	10 giorni	29/06/24 8.00	12/07/24 17.00		MORETTI					
2		SCAVI	15 giorni	15/07/24 8.00	02/08/24 17.00		MORETTI					
3		FONDAZIONI	20 giorni	05/08/24 8.00	30/08/24 17.00		MORETTI					
4		COSTRUZIONE MURI IN O...	15 giorni	05/08/24 8.00	23/08/24 17.00		MORETTI					
5		MONTAGGIO PREFABBRIC...	28 giorni	26/08/24 8.00	02/10/24 17.00		MORETTI					
6		POSA PAVIMENTAZIONE	20 giorni	03/10/24 8.00	30/10/24 17.00		MORETTI					
7		POSA SERRAMENTI	15 giorni	31/10/24 8.00	20/11/24 17.00		MORETTI					
8		POSA IMPIANTO SPRINKLER	30 giorni	31/10/24 8.00	11/12/24 17.00		MORETTI					
9		POSA COPERTURA	20 giorni	03/10/24 8.00	30/10/24 17.00		MORETTI					
10		POSA IMPIANTO ELETTRICO	20 giorni	31/10/24 8.00	27/11/24 17.00		MORETTI					
11		POSA IMPIANTO TERMICO	20 giorni	31/10/24 8.00	27/11/24 17.00		MORETTI					
12		POSA BAIE DI CARICO	10 giorni	31/10/24 8.00	13/11/24 17.00		MORETTI					

PROVINCIA DI Piacenza
 Ordine degli Architetti,
 Pianificatori,
 Paesaggisti e
 Conservatori


 CHIARA
 FIORANI
 Architetto 619







This document was created with the Win2PDF "print to PDF" printer available at <http://www.win2pdf.com>

This version of Win2PDF 10 is for evaluation and non-commercial use only.

This page will not be added after purchasing Win2PDF.

<http://www.win2pdf.com/purchase/>
